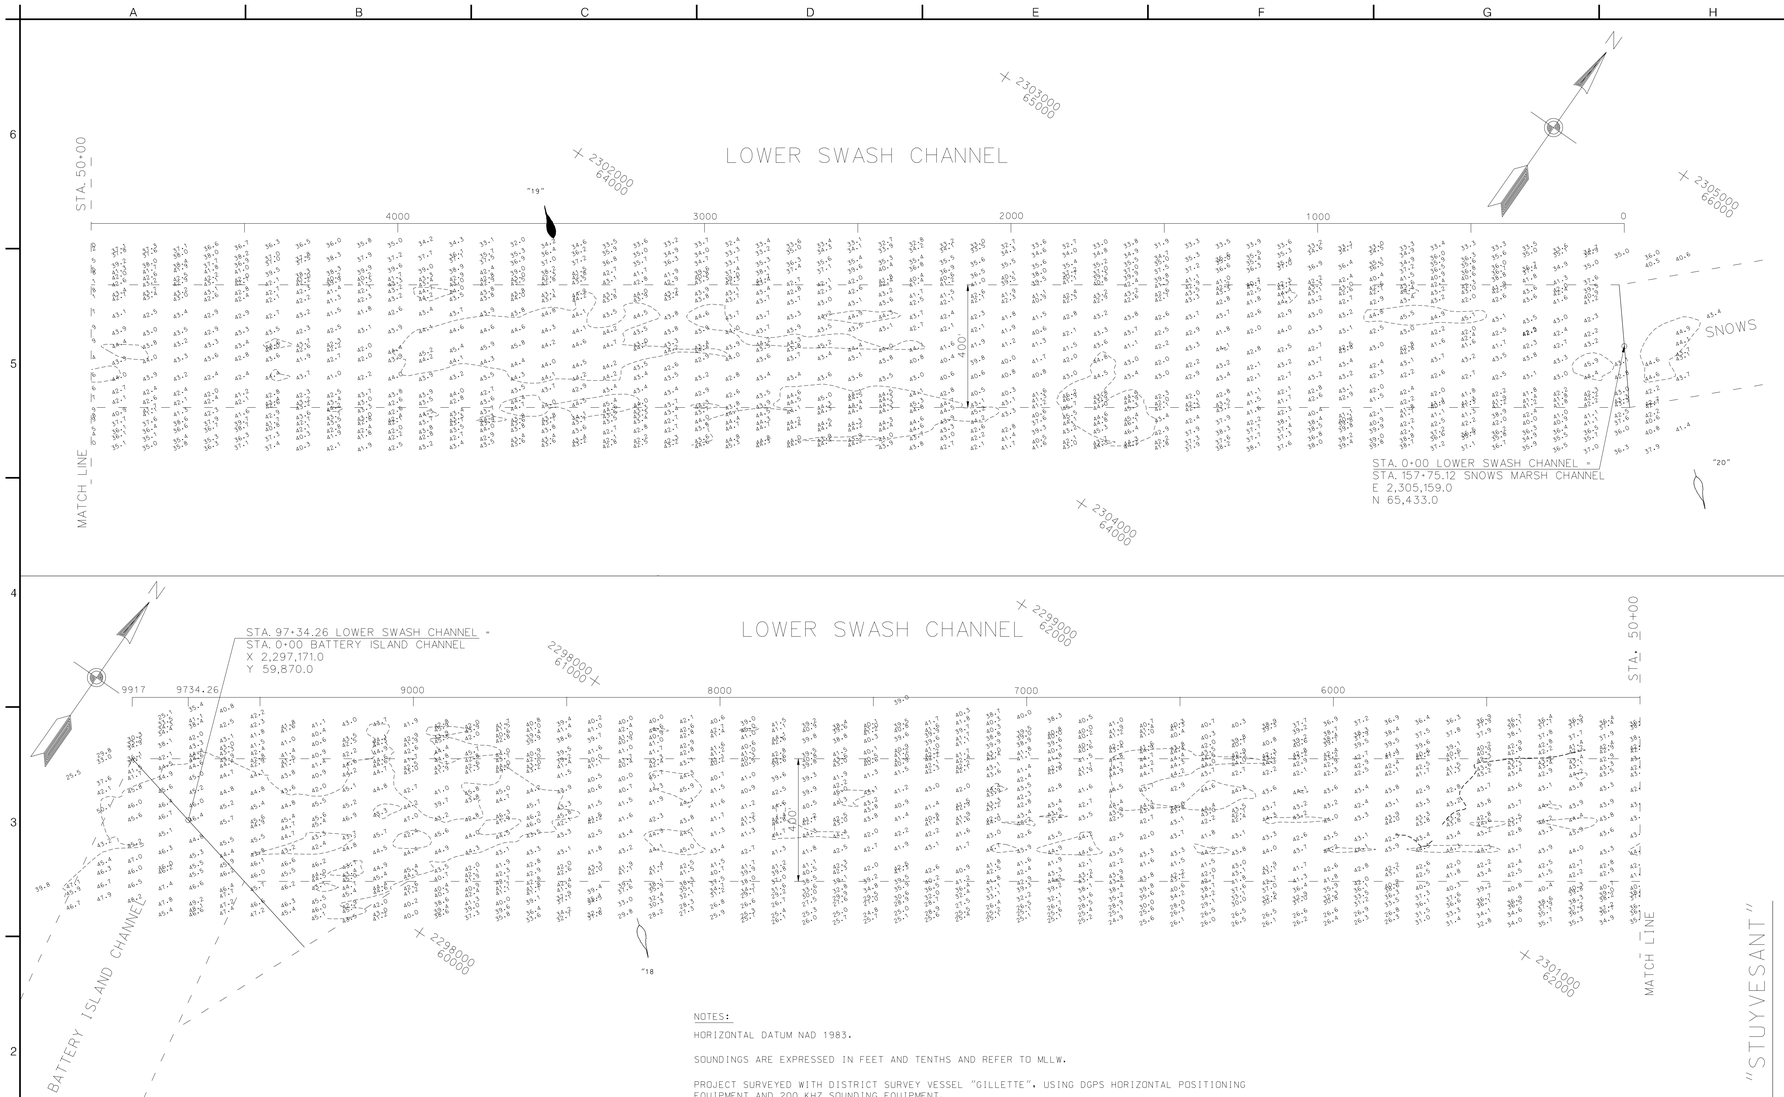

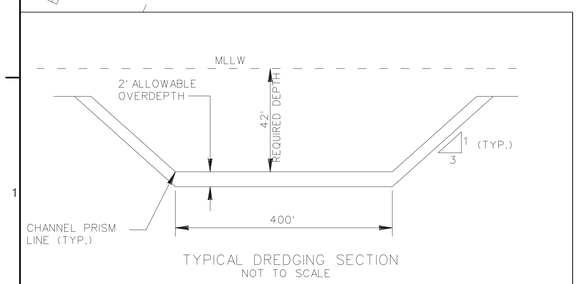

TYPICAL DREDGING SECTION
NOT TO SCALE

NOTES:

HORIZONTAL DATUM NAD 1983.

SOUNDINGS ARE EXPRESSED IN FEET AND TENTHS AND REFER TO MLLW.

PROJECT SURVEYED WITH DISTRICT SURVEY VESSEL "GILLETTE". USING DGPS HORIZONTAL POSITIONING EQUIPMENT AND 200 KHZ SOUNDING EQUIPMENT.

TIDE GAGE LOCATED AT - SOUTHPORT CITY DOCK AND PFIZER

THE INFORMATION DEPICTED ON THIS MAP REPRESENTS THE RESULT OF SURVEYS MADE ON THE DATE INDICATED AND CAN ONLY BE CONSIDERED AS INDICATING THE GENERAL CONDITIONS EXISTING AT THAT TIME.

NAVIGATION AIDS LOCATED WITH DISTRICT SURVEY VESSEL. ACCURACY PLUS / MINUS 3 METERS.

LT. BUOY	# 18	2298512	60306	LAT. 33.91162	LONG. 78.01628
LT. BUOY	# 19	2302110	63713	LAT. 33.92089	LONG. 78.00431
LT. BUOY	# 20	2305575	65233	LAT. 33.92497	LONG. 77.99284

THIS MAP SHOWS CONDITION OF CHANNEL AFTER DREDGING BY THE DREDGE "STUYVESANT". BEAN STUYVESANT DREDGING COMPANY DURING THE PERIOD FEBRUARY THRU APRIL 2001. FOR CONDITION OF CHANNEL PRIOR TO SEE MAP NO. WH 105-01-18. DATED 2 MARCH 2001.

SCALE: 1"=200'
500 400 300 200 100 0 500
SCALE IN FEET

AFTER DREDGING "STUYVESANT"

US Army Corps of Engineers
Wilmington District

SYMBOL	DESCRIPTION	DATE	APPROVED	SYMBOL	DESCRIPTION	DATE	APPROVED

SURVEYED BY: S.V. WWW
DRAWN BY:
CHECKED BY:
REVIEWED BY:
DATE: 2 JUNE 2001
APPROVED BY: DISTRICT ENGINEER BRANCH
MAP FILE NO. WH 105-01-72
SURVEYED: 31 MAY 2001
FILE NAME: LSWH151.DGN
PLOT SCALE: 1" = 200'

U.S. ARMY ENGINEER DISTRICT
CORPS OF ENGINEERS
WILMINGTON, NORTH CAROLINA

CONTRACT NO. DACW54-01-C-0012

WILMINGTON HARBOR, NC - 96 ACT
SNOWS MARSH, STA. 157+75 TO STA. 1+00 TRIBUTARY
SHOAL CHANNEL STA. 20+00 TO STA. 1+00 DREDGING

LOWER SWASH CHANNEL

PLATE NUMBER

SHEET OF

.../lswash/ad/lswh151.dgn Jul. 24, 2001 11:38:19
